


Software Implementation Planning — roadmap

Page 2/3 — Steps 5-8 · Plan: 55d original · ~5.1d actual to 26 Sep · ~47d remaining · ~1d/week · +25% reserve

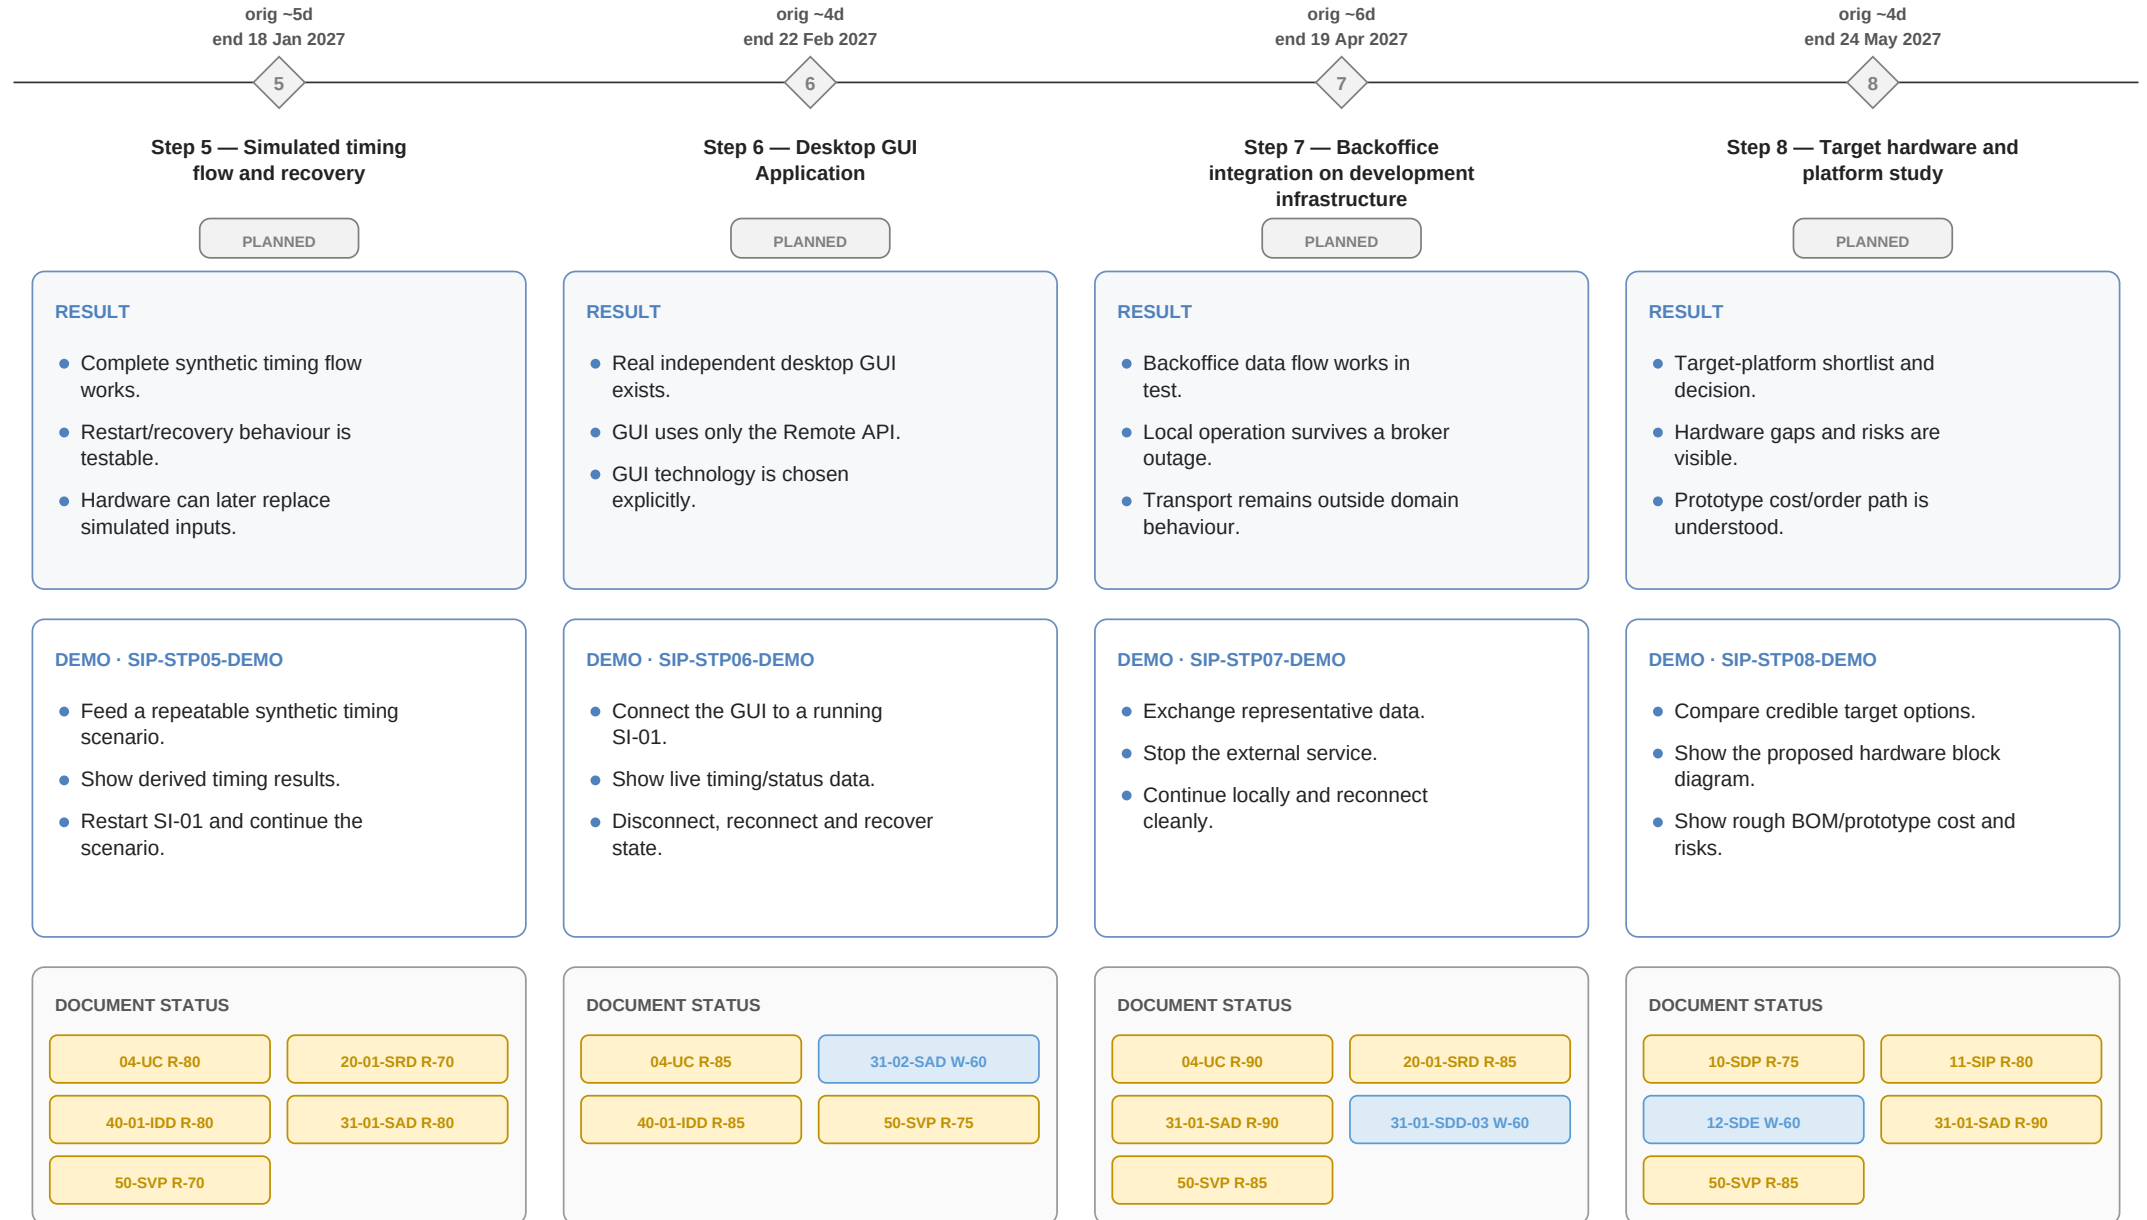

Software Implementation Planning — roadmap

orig ~4d
end 28 Jun 2027

9

orig ~8d
end 06 Sep 2027

10

orig ~8d
end 15 Nov 2027

11

Step 9 — Target bring-up and deployment proof

PLANNED

RESULT

- SI-01 runs on selected target hardware.
- Real runtime behaviour is measured.
- Deployment needs are known from use.

DEMO · SIP-STP09-DEMO

- Boot the target and start SI-01.
- Connect through Remote API/GUI.
- Show runtime observations and restart.

DOCUMENT STATUS

12-SDE R-75

31-01-SAD R-92

50-SVP R-88

60-01-SUM W-55

Step 10 — Real timing-device integration

PLANNED

RESULT

- Real timing devices use normal SI-01 paths.
- Device status/recovery is observable.
- Synthetic and real flows remain comparable.

DEMO · SIP-STP10-DEMO

- Run a representative real-device flow.
- Show timing data/results through the GUI.
- Demonstrate one device recovery case.

DOCUMENT STATUS

04-UC R-95

20-01-SRD R-95

31-01-SAD R-95

50-SVP R-95

60-01-SUM W-70

Step 11 — Integrated system and field proof

PLANNED

RESULT

- Representative integrated system works.
- Recovery paths are demonstrated.
- Remaining hardening work is evidence-based.

DEMO · SIP-STP11-DEMO

- Run a representative timing session.
- Interrupt one external dependency/device.
- Recover and complete the session.

DOCUMENT STATUS

04-UC A-95

20-01-SRD A-95

31-01-SAD A-95

50-SVP A-95

60-01-SUM A-90

11-SIP R-95
